


Red River Area Improvements

Monthly Virtual Project Updates



**Economic
Development**
CITY OF AUSTIN



**PUBLIC
WORKS**

Project Team

Economic Development

- Nicole Klepadlo, EDD Project Sponsor
- Donald Jackson, EDD Project Team
- Matthew Schmidt, EDD Project Team/Community Contact


ASD Consultants, Inc.

- Curtis Brown, Project Manager
- Anthony White, Project Superintendent
- Farid Wahidy, Office Engineer

Public Works

- Jose Ibarra, PW Project Manager
- Kevin Sweat, PW Project Team
- Kimberley Gilbertson, PW Project Team
- Christopher Newton, PW Project Team
- David Garcia, CMD Project Team
- Simon Orta, CMD Project Team
- William Power, CMD Project Team

Red River Area Improvements Project Information



**Economic
Development**
CITY OF AUSTIN

Project History

- [Resolution No. 20170608-033](#) directed the City Manager to explore a variety of public infrastructure enhancements along Red River Street.
- Stakeholder engagement meetings were completed to inform design and improvements by a collaborative effort by the City of Austin's Public Works Department (PWD) and Economic Development Department (EDD)

Scheduled Improvements:

- Sidewalk repairs and improvements
- Curb cuts and street alignment (9th Street)
- Pedestrian safety improvements
- Pedestrian scale solar lighting pilot
- Planters/landscaping (pending maintenance agreements)

Overall Project Timeline

Start of Construction: Began Mid-December 2021

End of Construction: Summer 2022

Expected Construction Hours:

- Sunday- Wednesday 7AM – 5PM
- Thursdays 7AM – 3PM
- No construction Fridays and Saturdays*
- Due to the restrictions on construction timing overall project may take longer with coordination of supplies and communication with businesses

*These proposed construction hours are subject to change

Construction hours are subject shift as we work directly with business owners at different stages of the projects


Completed Work: 600-700 Block of Red River

- Construction began within the 600-700 Block of Red River
- Improvements Completed:
 - Pedestrian Safety Improvements SW, SE, NE Corners of 7th and Red River
 - Partial curb closure of driveways adjacent to intersections
 - Sidewalk repair and improvements
 - Bus Stop Relocation



Completed Work: 7th Street Plaza/Curb Rehab

- Continued improvements to 7th Street Pedestrian Plaza
- 7th Street Curb Rehabilitation
- Improvements Completed:
 - Pedestrian Safety Improvements at NW Corner
 - Removal of “Double Sidewalk” and completion of wide pedestrian plaza
 - Driveway and Ramp Improvements on North side of Plaza
 - Curb Rehabilitation along 7th Street (Side Bar/Empire)

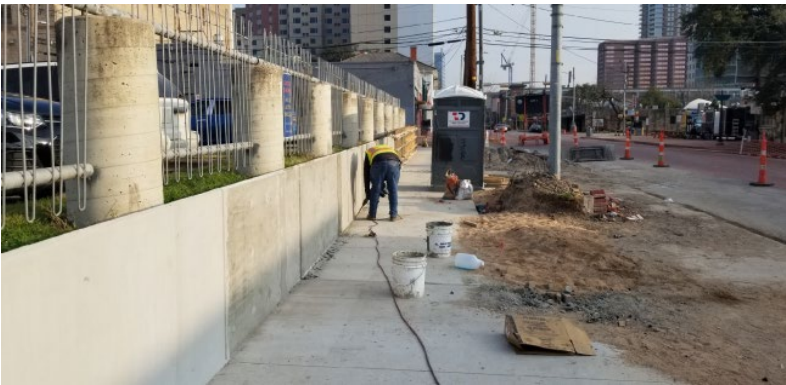

Expected Work: Next 30 Days

- Completion of 7th Street Plaza
 - Completion of Plaza Retaining Wall
 - Solar Light Installation
 - Plaza Clean-Up and Reopening
- 7th Street Improvements
 - Curb and Sidewalk Rehabilitation (Near Side Bar/Empire)
- Spring Festival Construction Moratorium
 - March 5th – March 22nd
 - Evaluation and planning for next steps

District Construction Signage



Construction Site Signage



Business Signage

Signs are available upon request from Cody (District Rep) or Matt (CoA Community Contact)

Project Contact Information

REGULAR UPDATES WILL BE PUBLISHED ON THIS PROJECT WEBSITE. WWW.AUSTINTEXAS.GOV/PAGE/RED-RIVER-AREA-IMPROVEMENTS

For questions or comments on these projects contact:

Jose Ibarra, Project Manager, Public Works Department

Jose.Ibarra@austintexas.gov | 512-974-7195

Nicole Klepadlo, Redevelopment Project Manager, Economic Development Department

Nicole.Klepadlo@austintexas.gov | 512-974-7739

Matthew Schmidt, Redevelopment Program Manager, Economic Development Department (*Community Contact*)

Matt.Schmidt@austintexas.gov | 512-974-6415


Cody Cowan, District Representative
cody@redriverculturaldistrict.org | 512-587-2369

THANK YOU!

Next Virtual Meeting:

Wednesday, March 30th

11:00AM-12:00PM



**Economic
Development**
CITY OF AUSTIN
