

Auditorium Shores Improvements Urban Forestry Board

Parks and Recreation Department CIP Project Management October 16, 2013



Outline



- Project History
- Current Schematic Design
- Project Phasing
- Construction Documents
 - Contractor Selection/Qualifications
- Project Milestones
- Next Steps



Town Lake Park – 2000 Master Plan



TOWN LAKE PARK



Jane 7th, 2000 San Plan Mett-2230c Interim

TEAMTEG



Town Lake Park – 2011 Master Plan





Auditorium Shores Improvements


Overall Schematic







Auditorium Shores Improvements Phasing Diagram

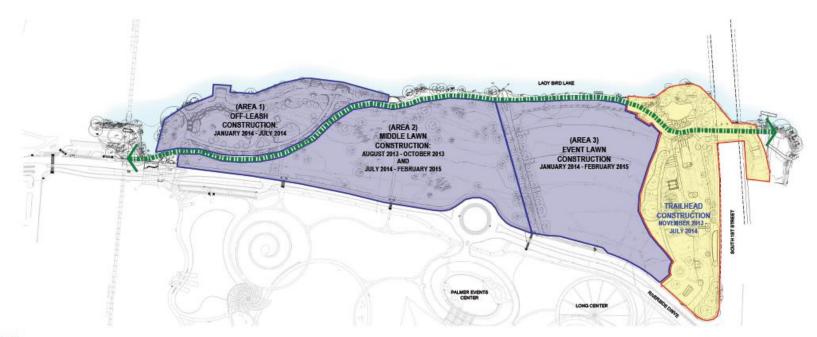


EGEND:

Auditorium Shores Trailhead
Auditorium Shores Imailhead
Auditorium Shores Improvements
AREA 1 = Off-Leash Area
AREA 2 = Widdle Lawn
AREA 3 = Event Lawn



its

Auditorium Shores Improvements Construction Documents and Permits

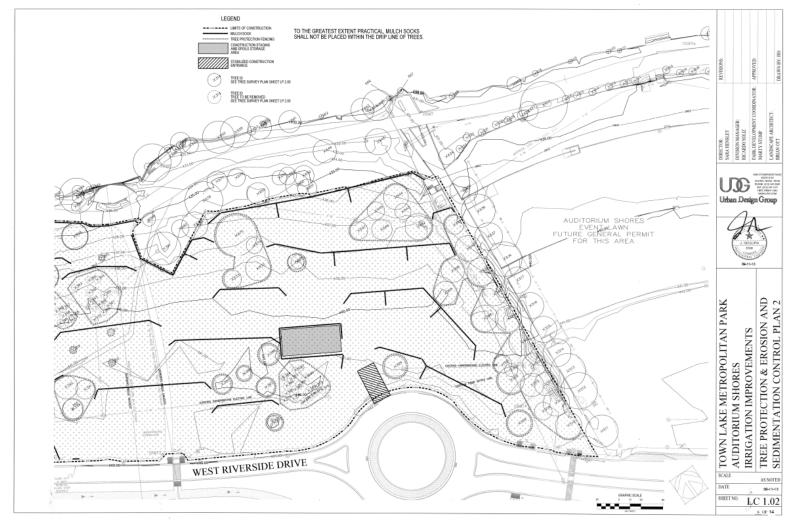



Project Milestones





PAST MILESTONES

- Briefing to Council -05-23-2013
- Auditorium Improvements Public Meeting #1 -07-10-2013
- Auditorium Improvements Public Meeting #2 -09-28-2013

FUTURE MILESTONES

- Parks and Recreation Board -November 2013
- Planning Commission -December 2013
- City Council Briefing -December 2013
- Approved Permit -January 2014
- Start of Construction -January 2014



Next Steps



- Overall Project Approvals
- Construction and Permit Documents
- Collaboration with PARD Forestry
- Phased Project Construction
- Final Public Re-opening Feb 2015

